



SOUTH COAST AQMD
CLERK OF THE BOARDS

April 1, 2016

CN: 15279

'16 APR -1 P1:47

Ms. Cher Snyder
Assistant Deputy Executive Officer
Office of Engineering and Compliance
South Coast Air Quality Management District
21865 Copley Drive
Diamond Bar, CA 91765

**PROJECT: EXIDE TECHNOLOGIES FACILITY ID NO. 124838,
ORDER OF ABATEMENT CASE NO. 3151-32**
RE: WEEKLY STATUS REPORT # 80 (3/17/16 – 3/23/16)

Dear Ms. Snyder,

Tetra Tech Inc. is pleased to present the following Weekly Status Report for the above referenced project. This report covers the period of March 17, 2016 through March 23, 2016.

CURRENT ACTIVITIES WHERE PREVIOUSLY APPROVED MITIGATION MEASURES WERE FULLY IMPLEMENTED

Major items of work performed by Exide and/or its contractor(s) (including specific mitigation measures) during this reporting period where mitigation measures were observed to be implemented in full compliance with the previously approved mitigation measures under the Mitigation Plan for RCRA RFI Sampling, and Other Plant Activities or other Mitigation Plans, as approved by the SCAQMD, at the site during this period include:

TASK ID	Major Work Item	Mitigation Measure(s)
EX83/4	RCRA RFI Soil Sampling	Temporary Enclosure Under Negative Pressure
EX115	Sediment Removal from Equalization Tanks	Maintain Wetted Surfaces
EX114	Replace WWTP Clarifier Chevrons	Maintain Wetted Surfaces

* Dust Trak monitoring performed for this work item.

RCRA RFI Soil Sampling

No work occurred related to the RCRA RFI Soil Sampling. RCRA RFI Soil Sampling activities on the Exide property will continue once a revised scope of work to address changed field conditions is developed and approved by the regulatory agencies.

Sediment Removal from Equalization Tanks

No work occurred related to the sediment removal from the Equalization Tanks. Removal of sediment from Equalization Tank #1 will occur during a future reporting period when it will not impact water treatment activities.

Replace WWTP Clarifier Chevrons

No work occurred related to the replacement of WWTP Clarifier Chevrons during this reporting period. Replacement of the remaining chevrons is scheduled to resume during the next reporting period.

CURRENT ACTIVITIES WHERE A DEVIATION FROM PREVIOUSLY APPROVED MITIGATION MEASURES WERE OBSERVED AND THE CORRECTIVE ACTIONS TAKEN

Major items of work performed by Exide and/or its contractor(s) (including specific mitigation measures) currently under way or completed during this reporting period where for each of the activities described below, mitigation measures were implemented which to some extent deviated from the previously approved mitigation measures under the Mitigation Plan for RCRA RFI Sampling, and Other Plant Activities or other Mitigation Plans, as approved by the SCAQMD:

TASK ID	Major Work Item	Deviation(s)	CORRECTIVE ACTION
None			

In general accordance with the Order for Abatement Case No. 3151-32 Findings and Decision, air monitoring, if required, was conducted during a portion of all repair work performed within the temporary enclosures on a daily basis. If the results of continuous Dust Trak air monitoring detected excessive dust, additional suppression activities are required to be implemented. For this reporting period, Dust Trak monitoring did not detect excessive dust being generated from repair activities.

Activity Which Resulted in Excessive Dust	Additional Suppression Activity
None	None

ACTUAL vs. FORECAST PROGRESS:

Exide Technologies submitted a schedule which outlines the tasks needed to be completed in response to this abatement order. The attached Gant Chart shows scheduled progress for all activities planned for the upcoming two week period. The following table shows the status of these activities.

TASK	STATUS
None	None

WORK SCHEDULED DURING THE UPCOMING PERIOD:

The following activities are anticipated for the upcoming weeks:

Week	Anticipated Activities
Mar. 24 – Mar. 30	<ul style="list-style-type: none">• Replace WWTP Clarifier Chevrons Resumes• Installation of Well Box on Former Production Well

Week	Anticipated Activities
Mar. 31 - Apr. 6	<ul style="list-style-type: none">• Replace WWTP Clarifier Chevrons Completes• Installation of Well Box on Former Production Well Completes

KEY MILESTONES:

The following key milestones were achieved during this reporting period:

- o None at this time.

WORKER SAFETY CONCERNS:

The following Health and Safety issues, as they apply to Tetra Tech employees, were observed during this reporting period:

- o None.

POTENTIAL CHANGES AND ACTION ITEMS REQUIRING RESOLUTION:

The following items require resolution:


- o None at this time.

SUMMARY:

The summary provided herein covers the activities for the period of March 17, 2016 through March 23, 2016. Tetra Tech personnel were not onsite during this reporting period other than for regularly schedule meetings, as no mitigation plan work was scheduled. Please find attached a copy of Exide’s upcoming two weeks schedule and site map identifying the location of the activities on the upcoming two weeks schedule.

Should you have questions regarding this report, or require additional information, please contact me at your earliest convenience.

Sincerely,



Nick Somogyi *Nir*
Project Engineer

ATTACHMENTS:
Gant Chart Schedule
Site Map

Gant Chart Schedule

Project Schedule

Week of 03/16/16 – 04/07/16

Rev: 03/24/2016



Recycling Division, Vernon, CA

							3/19/2016			03/26/16					04/02/16				04/09/16										
Mitigation Plan Risks	Task Name	Plant Location	Duration	Start Date	Finish Date	%	16	17	18	19	20	21	22	23	24	25	26	27	28	29	30	31	01	02	03	04	05	06	07
Ex 72	Cleaning of Assorted Materials in Total Enclosure	Total Enclosure	497 days	11/20/14	3/31/16	80%																							
Ex 76	Various Work Methods in Total Enclosure	Total Enclosure	496 days	11/21/14	3/31/16	80%																							
4	RCRA RFI Soil Sampling	General	407 days	2/18/15	3/31/16	97%																							
Ex 83	RFI Soil Sampling Supplemental	General	407 days	02/18/15	3/31/16	97%																							
Ex 114	Replace WWTP Clarifier Chevrons	WWTP	4 days	3/16/16	03/31/16	20%																							
Ex 112	Installation of Well Box on Forner Production Well	South Yard	4 days	3/28/16	03/31/16	0%																							

*Numbering system correlates with Mitigation plan document.
Ex refers to additional work part of Sec. 6b in the Mitigation plan document.*

Site Map



Mitigation Project Map Layout

Week 03/16/16 – 04/01/16

Rev: 03/24/16

4. RCRA RFI Soil Sampling


Ex 83. RFI Soil Sampling Supplemental

Ex 72. Cleaning of Assorted Materials in Total Encl.

Ex 76. Various Work Methods in Total Enclosure

Ex 114 Replace WWTP Clarifier Chevrons

Ex 112 Installation of Well Box

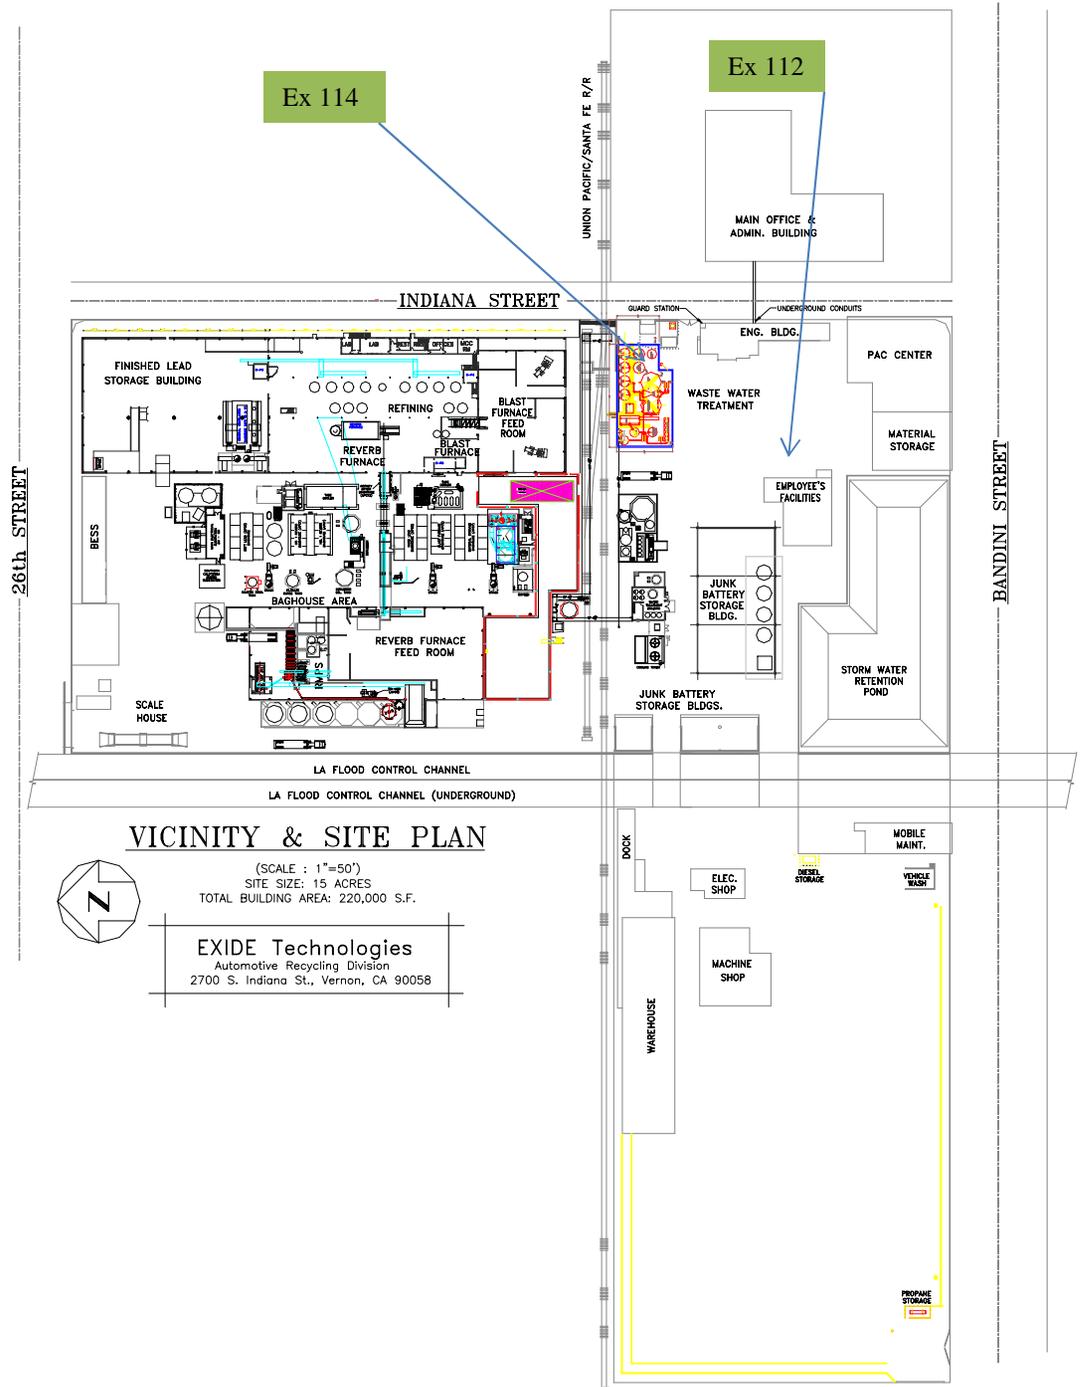

Numbering system correlates with Mitigation plan document. Ex refers to additional work part of Sec. 6b in the Mitigation plan document.

Mitigation Schedule and Map_03/24/16.pptx
